Cabinet-in-Confidence

Attachment A2

East West Link Stage One
Combined project schedule - LMA, DTPLI, VicRoads
(PPR-Relevant Extract)
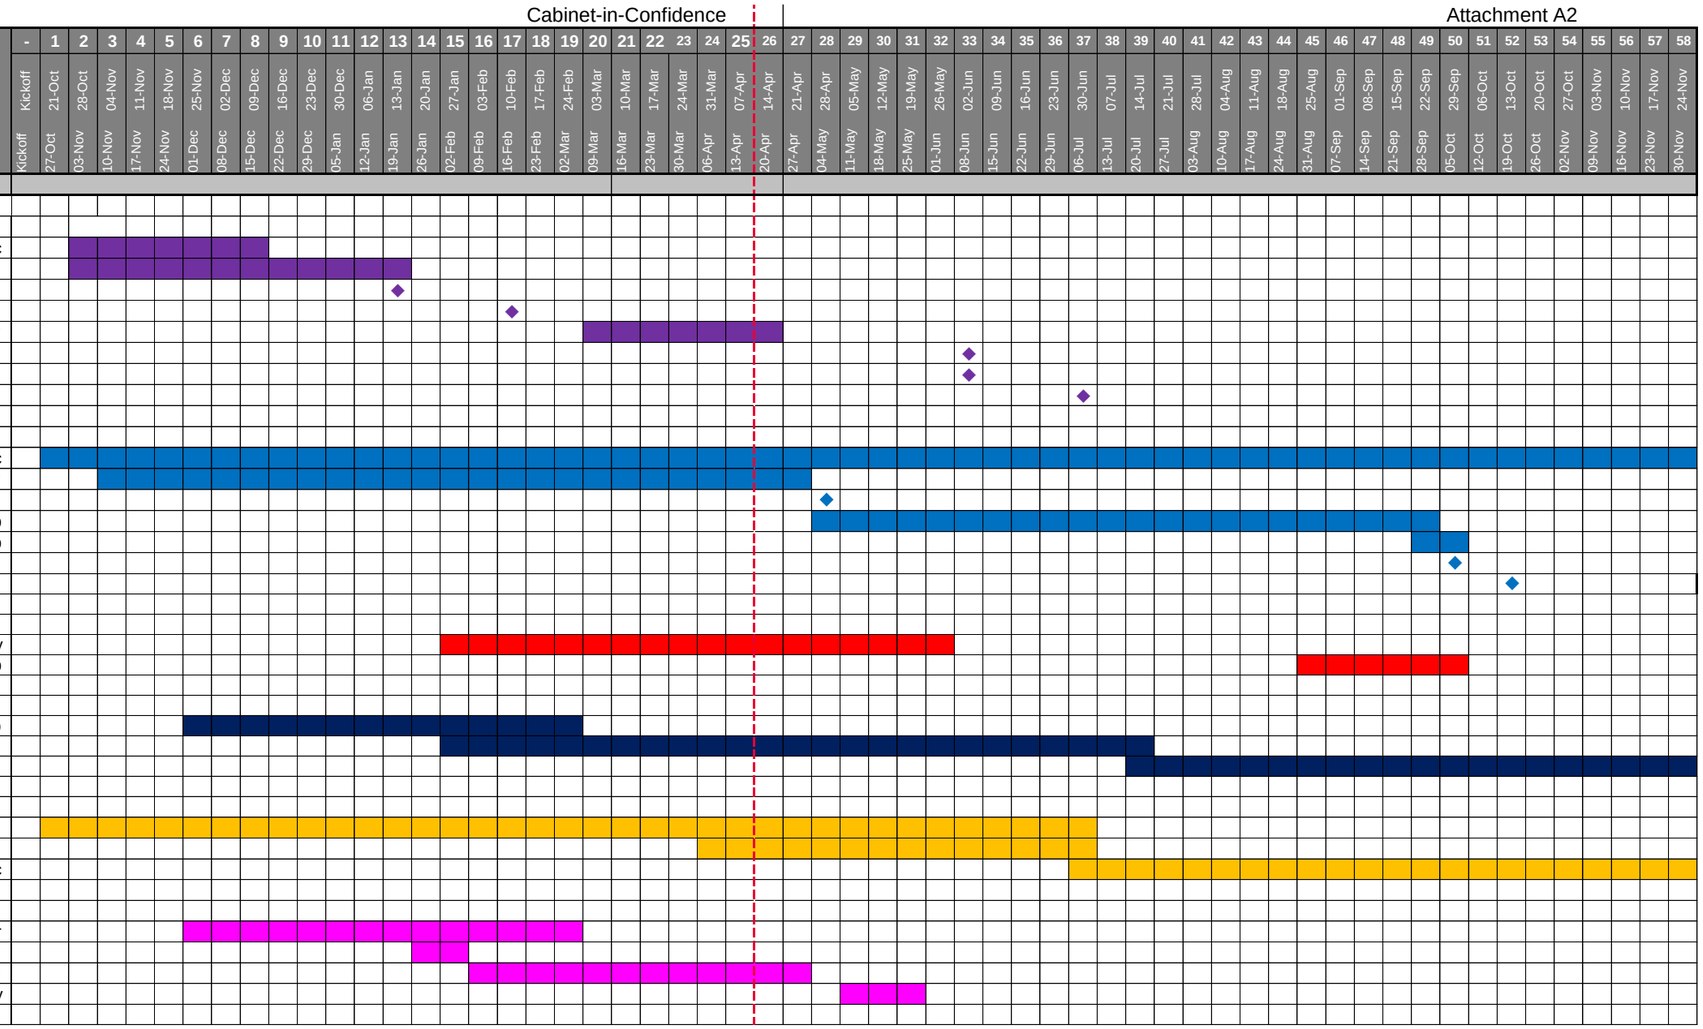
	Agency	Start	Finish
CIS	**LMA**		
Exhibition of CIS		31-Oct	12-Dec
Assessment of CIS submissions		31-Oct	14-Jan
Preliminary Hearing		14-Jan	
LMA response to Assessment Committee Request		11-Feb	
Public Hearing		05-Mar	15-Apr
EPA advice on to Planning Minister on Works Approval (est.)		02-Jun	
Assessment Committee recommendation to Planning Minister		02-Jun	
Ministerial decision (est.)		01-Jul	
RFP	**LMA**		
Probity and conflict management		21-Oct	31-Dec
Interactive tender phase		07-Nov	28-Apr
RFP Bid Submission Date		28-Apr	
Evaluation		28-Apr	26-Sep
Approvals		26-Sep	30-Sep
Contract Close (est.)		30-Sep	
Financial Close (est.)		17-Oct	
Independent Reviewer Appointment	**LMA**		
Preparation and EOI		31-Jan	31-May
Appointment		31-Aug	30-Sep
Early Works - shared user overpass Eastern Freeway	**LMA**		
Design development		29-Nov	28-Feb
Procurement process		01-Feb	18-Jul
Design and construction phase		19-Jul	31-Jan
Land Acquisition	**LMA**		
Preparing statutory docs for State and Crown Land order		21-Oct	01-Jul
Document preparation for private land acquisiton		01-Apr	01-Jul
Commence land acquisition (following CIS approval)		02-Jul	31-Dec
Integrated and Enabling Projects	**DTPLI/VR**		
Business case development		01-Dec	01-Mar
HVHR Gateway review		24-Jan	31-Jan
DTPLI / DTF Internal review		01-Feb	30-Apr
BERC consideration		12-May	31-May
